Activity ID	Activity Name	Start	Finish	Original Duration
Scappoose Industrial Subdivision		**17-Oct-19 A**	**21-Feb-20**	**73d**
Milestone Dates				**0d**
Utilities		**17-Oct-19 A**	**21-Feb-20**	**73d**
Sewer				**0d**
Storm				**0d**
Water				**0d**
Columbia Street Sewer		**17-Oct-19 A**	**21-Feb-20**	**88d**
A2080	Set Up Traffic Control	17-Oct-19 A	22-Oct-19 A	4d
A2085	Install Temp Access Along Shoulder	23-Oct-19 A	25-Oct-19 A	3d
A2090	Meet and Greet	29-Oct-19 A		0d
A2100	Phase 1 Install SSMH H1 to NE 14th Street	30-Oct-19 A	27-Nov-19	14d
A2110	Phase 2 Install SSMH H4 to Miller Street	27-Nov-19	10-Dec-19	7d
A2120	Phase 3 Install SSMH H6 to Tyler Street	10-Dec-19	19-Dec-19	7d
A2130	Phase 4 Install SSMH H7 to Bird Road	19-Dec-19	31-Dec-19	7d
A2140	Phase 5 Tie in EX MH J1 and Waste Water Faci	31-Dec-19	06-Jan-20	3d
A2142	Tie in EX MH NE 14th and Miller	06-Jan-20	09-Jan-20	3d
A2145	Tie In EX MH J7 at Tyler St	09-Jan-20	14-Jan-20	3d
A2147	Tie In Ex MH K1 and J8 at Bird Road	14-Jan-20	20-Jan-20	4d
A2148	Testing	20-Jan-20	27-Jan-20	5d
A2150	Tie in Laterals Tax Lots 3100, 3200, 3300 and 3	27-Jan-20	31-Jan-20	4d
A2160	Tie in Laterals Tax Lots 1100, 501, 102, 102,	31-Jan-20	06-Feb-20	4d
A2165	Tie in Any Unknown Laterals from South Side	06-Feb-20	10-Feb-20	2d
A2170	Abandon Existing Sewer Line	10-Feb-20	17-Feb-20	5d
A2180	Cleanup and Pave Back Sewer Trench	17-Feb-20	21-Feb-20	4d
Roadwork				**0d**
LIDA and Pond				**0d**
Streets				**0d**
Parking Lot, Path, Approaches, and Pond Access Roa				**0d**
Sidewalk, Approaches and ADA				**0d**
Restroom (Filler Work)				**0d**
Landscape				**0d**

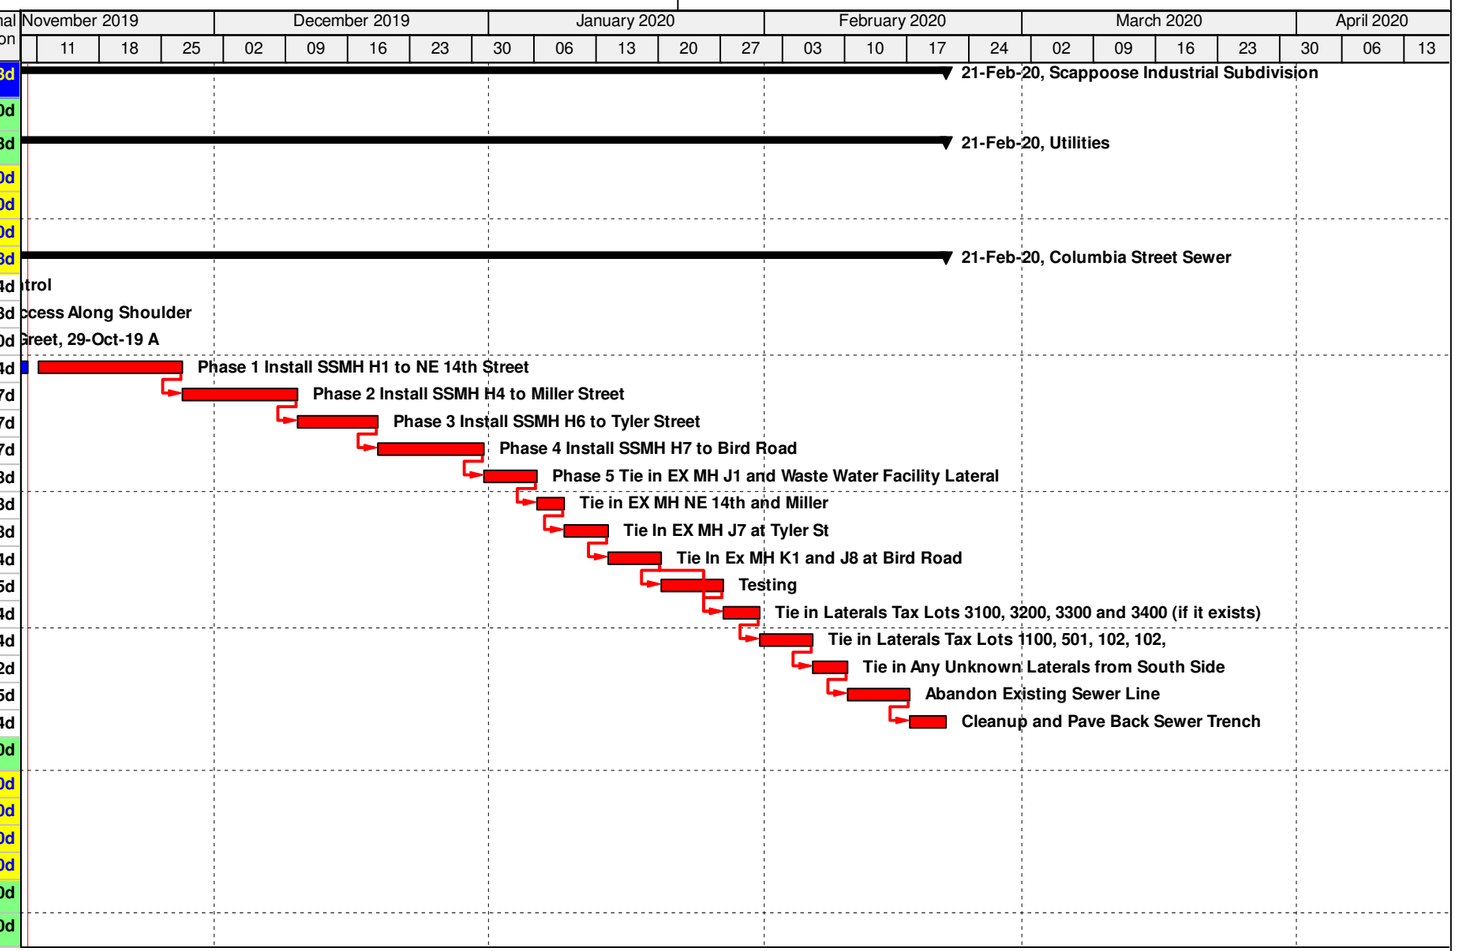

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: (Untitled Filter).

© Oracle Corporation
