Activity ID	Activity Name	Start	Finish	Original Duration
Scappoose Industrial Subdivision		17-Oct-19 A	27-Feb-20	77d
Milestone Dates				0d
Utilities		17-Oct-19 A	27-Feb-20	77d
Sewer				0d
Storm				0d
Water				0d
Columbia Street Sewer		17-Oct-19 A	27-Feb-20	92d
A2080	Set Up Traffic Control	17-Oct-19 A	22-Oct-19 A	4d
A2085	Install Temp Access Along Shoulder	23-Oct-19 A	25-Oct-19 A	3d
A2090	Meet and Greet	29-Oct-19 A		0d
A2100	Phase 1 Install SSMH H1 to NE 14th Street	30-Oct-19 A	05-Dec-19	14d
A2110	Phase 2 Install SSMH H4 to Miller Street	06-Dec-19	16-Dec-19	7d
A2120	Phase 3 Install SSMH H6 to Tyler Street	17-Dec-19	26-Dec-19	7d
A2130	Phase 4 Install SSMH H7 to Bird Road	27-Dec-19	07-Jan-20	7d
A2140	Phase 5 Tie in EX MH J1 and Waste Water Faci	08-Jan-20	10-Jan-20	3d
A2142	Tie in EX MH NE 14th and Miller	13-Jan-20	15-Jan-20	3d
A2145	Tie In EX MH J7 at Tyler St	16-Jan-20	20-Jan-20	3d
A2147	Tie In Ex MH K1 and J8 at Bird Road	21-Jan-20	24-Jan-20	4d
A2148	Testing	27-Jan-20	31-Jan-20	5d
A2150	Tie in Laterals Tax Lots 3100, 3200, 3300 and 3	03-Feb-20	06-Feb-20	4d
A2160	Tie in Laterals Tax Lots 1100, 501, 102, 102,	07-Feb-20	12-Feb-20	4d
A2165	Tie in Any Unknown Laterals from South Side	13-Feb-20	14-Feb-20	2d
A2170	Abandon Existing Sewer Line	17-Feb-20	21-Feb-20	5d
A2180	Cleanup and Pave Back Sewer Trench	24-Feb-20	27-Feb-20	4d
Roadwork				0d
LIDA and Pond				0d
Streets				0d
Parking Lot, Path, Approaches, and Pond Access Roa				0d
Sidewalk, Approaches and ADA				0d
Restroom (Filler Work)				0d
Landscape				0d

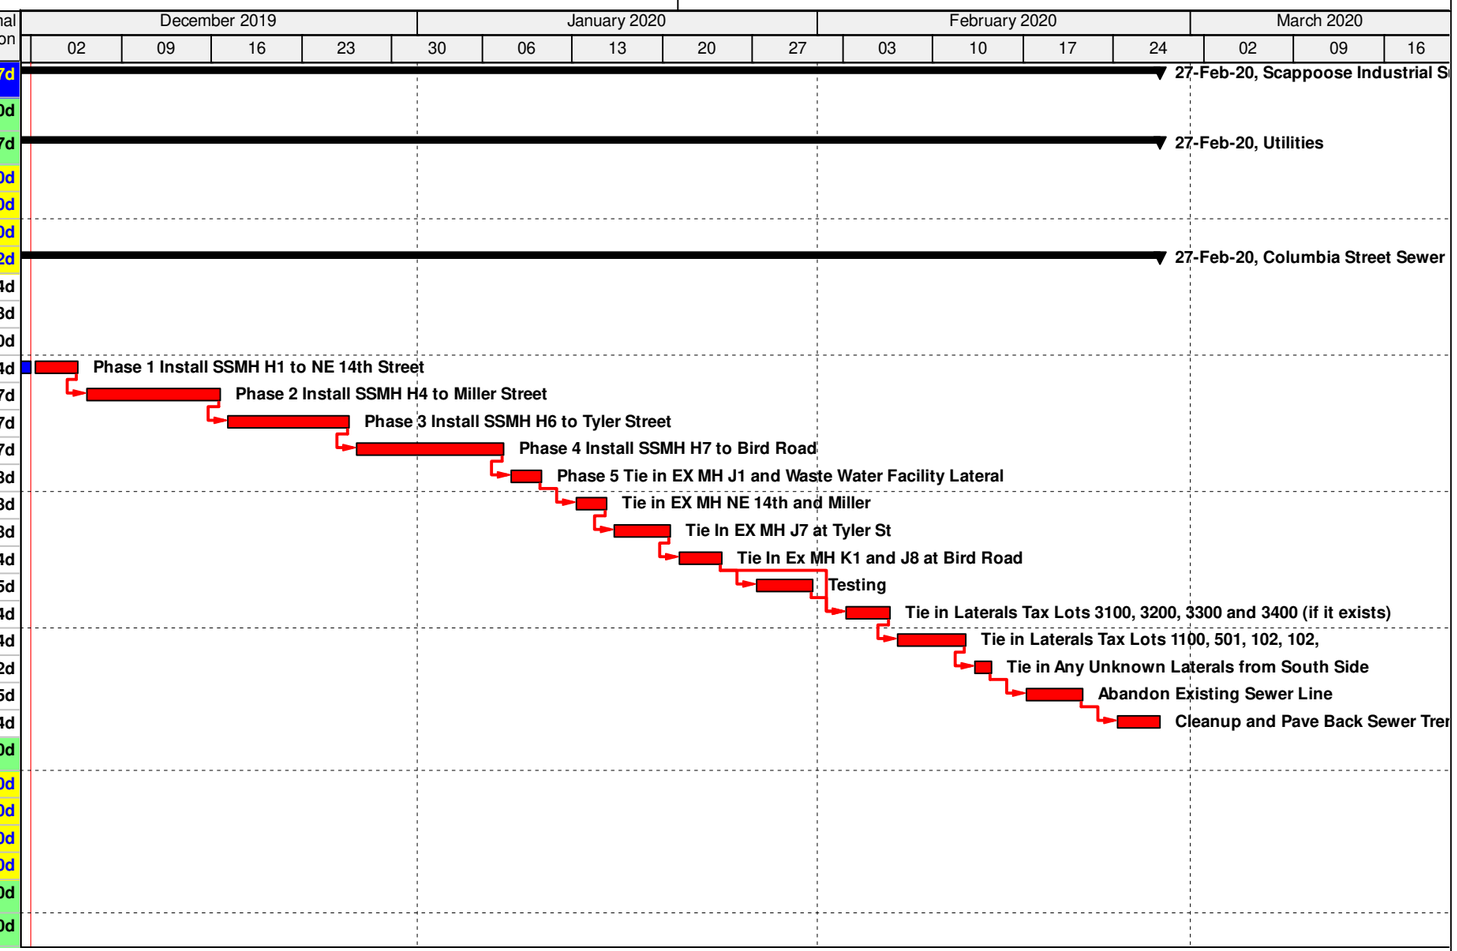

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: (Untitled Filter).

© Oracle Corporation
